

RPP -Sathyamoorthy (JV)

S.F.No..454, Ragupathynaiken palayam,
Poondurai Main Road,
Railway Colony post,
Erode – 638002
GST : 22ABCFR8363C1ZF
Email – raipur.rppvscjv@rppipl.com

Lr. No. RPP-SM-JV/RRW/462

Date: 01-07-2025

To,
The Authority's Engineer,
The Team Leader,
M/s Aarvee Associates Architects Engineers & Consultants Pvt. Ltd
8-2-5, ravula Residency, Srinagar Colony Main Rd
Hyderabad 500082
Telangana, India
Email: aarvee@aarvee.net

Dear Sir,

Project: Major up gradation of Raipur Railway Station of SECR on Engineering Procurement and Construction (EPC) mode.

Subject: Submission of MPR for June - 2025

References:

1. LOA issued vide Lr No: Raipur Division – Gati Shakti / DyCE-GSU-R-T-18- 23-24/00634660101437 dt 20-Apr-24.
2. EPC Contract Agt No: SECR/R/GS/2024/0005 dt 03-Jul-24.

1. In terms of clause 11.7 of the EPC contract (page 61), MPR for the month of June-2025 is hereby submitted.

2. Highlights of Jun – 2025

- 1.) 9B/19E excavation 63 Cum completed.
- 2.) 9B/19E waterproofing 221 Sqm completed.
- 3.) 9B/19E PCC 31 Cum (8 Nos) completed.
- 4.) 9B/19E foundation concrete 174.5 Cum (9 Nos) completed.
- 5.) 9B/19E 1st lift retaining wall 10 Rmt completed.
- 6.) 9B/19/E 8 Nos of 1st lift column completed.
- 7.) 9B/19/E 8 Nos of 2nd lift column completed.
- 8.) 19C RCC Foundation Concrete 220.75 cum (15 Nos) Completed.
- 9.) 19C Column Starter 15 Nos Completed.

- 10.) 19C Column 1st Lift 5 Nos Completed.
- 11.) RPF Colony 25 Nos of tree treatment completed.
- 12.) 4 No of Tree Shifting Completed at City Side.
- 13.) City Side UTS/PRS Location wiring work Testing and commissioning is completed.
- 14.) Rear Side (RHS) 480 Rmt. Embankment top completed.
- 15.) Rear Side 480 Rmt. Subgrade 1st layer completed.
- 16.) Rear Side (RHS) 380 Rmt. Subgrade 2nd layer completed.
- 17.) Rear Side (LHS) 50 Rmt. Subgrade 2nd layer completed.
- 18.) Rear Side 105 Rmt. Drain PCC Completed.
- 19.) Rear Side 230 Rmt. Drain Raft Completed.
- 20.) Rear Side (RHS) 360 Rmt. G.S.B Bed Completed.
- 21.) Rear side (RHS) 360 Rmt WMM Bed Completed.
- 22.) Engineering Colony feeder & DRM office feeder are underground modification completed with double 2 pole structure.
- 23.) For UTS PRS city side (50 sqmm X 4 core LT XLPE cable)2 length laying completed.
- 24.) Rear Side 36 Rmt. GI pipe 200 mm laying work completed.
- 25.) Rear Side 197 Rmt. GI pipe 50 mm laying work completed.
- 26.) Rear Side 114 Rmt. GI pipe 80 mm laying work completed.
- 27.) Rear Side 78 Rmt. GI pipe 50 mm Dismantling work completed.
- 28.) Rear Side 36 Rmt. GI pipe 40 mm Dismantling work completed.
- 29.) Rear Side 20 Rmt. GI pipe 100 mm Dismantling work completed.
- 30.) Loco Colony Rear Side 36 Rmt. DI pipe 200 mm laying work completed.
- 31.) Temporary Parcel Office City Side Work in Progress.
- 32.) UTS/PRS Rear Side Successfully Handover.
- 33.) 22 Nos TBT (Tool Box Talk) Completed.
- 34.) 11 Nos of Safety Induction Training Provided.
- 35.) There is no any Near Miss happened at site.
- 36.) First Aid Used Nos 1

3. Progress upto the end of Jun - 2025.

- 1) 9B/19E excavation 19371 Cum completed.
- 2) 9B/19E waterproofing 6236 Sqm completed.
- 3) 9B/19E PCC 673.75 Cum completed.
- 4) 9B/19E foundation concrete 2802.27 Cum (91 Nos) completed.
- 5) 9B/19E 1st lift retaining wall 220.3 Rmt completed.
- 6) 9B/19E 2nd lift retaining wall 55 Rmt completed.
- 7) 9B/19E 77 Nos of 1st lift Column completed.
- 8) 9B/19/E 46 Nos of 2nd lift column completed.
- 9) 19F/OHE-PSI -TRD office 2264 Cum excavation completed.
- 10) 19F OHE-PSI-TRD office 80.75 Cum PCC completed.
- 10.) 19G/RPF Barrack (Male) 2600 Cum excavation completed.
- 11.) 19G/RPF Barrack (Male) 81 Cum PCC completed.
- 12.) 19C Foundation Concrete 220.75 Cum (15 Nos) completed.

- 13.) 19C 5 Nos of Column completed.
 - 14.) 19C/Crew lobby office & TTE Rest room 4000 Cum excavation completed.
 - 15.) 19C/Utility Shifting 55 Rmt. GI Pipe 40 mm dismantling completed for 19 C Building Excavation work.
 - 16.) City Side UTS/PRS Location structure work completed.
 - 17.) City Side UTS/PRS Location wiring work Testing and commissioning is completed.
 - 18.) Rear Side UTS/PRS Successfully Handover.
 - 19.) RPF Colony 60 Nos of tree treatment completed.
 - 20.) Rear Side 780 Rmt. Embankment top completed.
 - 21.) Rear Side 780 Rmt. Subgrade 1st layer completed.
 - 22.) Rear Side (RHS) 380 Rmt. Subgrade 2nd layer completed.
 - 23.) Rear Side (LHS) 50 Rmt. Subgrade 2nd layer completed.
 - 24.) Rear Side (RHS) 360 Rmt. G.S.B Bed Completed.
 - 25.) Rear side (RHS) 360 Rmt WMM Bed Completed.
 - 26.) Rear Side 230 Rmt. Drain Footing RCC Completed.
 - 27.) Rear Side 455 Rmt. Drain PCC Completed.
 - 28.) Rear Side 3600 Rmt. HDPE pipe laying completed.
 - 29.) Rear Side 3987 Rmt. HT cable laying completed.
 - 30.) For UTS PRS city side (50 sqmm X 4 core LT XLPE cable)2 length laying completed.
 - 31.) Rear Side 20 Rmt. DI pipe 200 mm excavation completed.
 - 32.) Rear Side 36 Rmt. DI pipe 200 mm laying work completed.
 - 33.) Temporary Parcel Office City Side Work in Progress.
 - 34.) 47 Nos TBT (Tool Box Talk) Completed.
 - 35.) 18 Nos of Safety Induction Training Provided.
 - 36.) There is no any Near Miss happened at site.
 - 37.) First Aid Used Nos 1
4. **Financial Progress:** RA Bill 01 has been finalized (payment yet to be received) and RA Bill 02 is currently under review. The first RA bill for tree translocation has also been submitted. A total financial progress of ₹11.14 crore has been achieved up to June 2025
5. **Physical Progress:** 3.24% Physical Progress is achieved up to end of June - 2025.

Position of works at the end of June-2025 is as under:

Item No (as per Sch-G)	Item	Status
2.1	City Side Stn Bldg (1)	<ul style="list-style-type: none"> • Geo-Tech Investigations done. • Preliminary Drawings approved. • To shift the PRS/UTS, temporary PRS facility is constructed but despite rigorous follow up by us and the GSU, Open line S&T is not permitting to operationalize the facility. Now, the Commercial department has also given certain observations. Unfortunately, GSU had not involved them till now and the shifting is delaying further due to this reason.
2.2	Rear Side Stn Bldg (1A)	<ul style="list-style-type: none"> • Geo-Tech Investigations done. • Preliminary Drgs approved. • 2/4-wheeler parking in 1A is shifted to a temporary location. However, parking is shifted back to 1A as directed by AE for resurfacing of the temporary parking area. And temporary parking area black top surfacing done. • To shift the infringing PRS/UTS facility, temporary PRS/UTS facility developed. The same will be commissioned and work in 1A will be started with increased pace after the cable route plan for temporary PRS/UTS is approved. (Ref: Contractor's Lr No: 303 dt 28-April-25). • Extent area made available on date is barricaded and UG utility's location is in progress. • Final drawings of building were submitted to the Authority Engineer on 23rd April'2025. AE's Architect provided observations on 10.05.2025 & AE's HVAC observations received on 12.05.2025. Then AE provided observations of Plumbing & firefighting on 15.05.2025. • Re-Submission of Architecture Definitive Drawings for the Rear side Station Building 1-A. (Ref-Lr. No. RPP-SM-JV/RRW/457 dt 28-06-2025

Item No (as per Sch-G)	Item	Status
2.3	Departure/Air Concourse.	<ul style="list-style-type: none"> • Preliminary drawing of Departure Concourse is approved. • After, approval for change of scope for shifting OHE masts and other utilities is accorded (Ref: Contractor's Lr No: 270 dt 08-April-25), the further process will start. • Dwg submitted on 10.06.2025 • Comments received by AE on 18.06.2025
2.4	9A-MMTH (City Side)	<ul style="list-style-type: none"> • Preliminary Drgs Approved. • Vide DRM meeting dated 23rd April'2025 the decision to make this building without basement or with only one basement (depending on the site conditions) is taken. • The planning of the building is underway

2.5	<p>9B-MMTH (Rear Side). (MMTH + P Way Store + OHE + Crew Lobby + RPF Office).</p>	<ul style="list-style-type: none"> • Preliminary drawings for the building were approved. • Final drawing for the foundation of this building was also approved. • Execution of only 60 -70% foundation is possible because the rear side road is passing across the building. • Foundation concreting in progress. • Progress is slow due to presence of a road passing across this plot. This will be demolished after the diversion road is constructed. For diversion road, plan and profile submitted to AE vide Lr No: 273 dt 11-April-25 and AE have given list of the observations on this on 19.04.2025. • The complete set of drawings was submitted to the AE on 10-April-2025. • Discussions were held between PMS and the Contractor's Consultant on 29-April-2025, 30-April-2025, and 1-May-2025. • The Contractor submitted the BIM model to the authorities on 6-May-2025. • The Contractor received a letter from the AE's office on 9-May-2025. • The Contractor submitted a reply letter and structural drawings to the AE on 10-May-2025. • ARC (Architectural) comments were provided by the AE on 21-May-2025, and HVAC comments were provided on 22-May-2025. • One-on-one discussions were held from 20-May-2025 to 23-May-2025. • After incorporating these comments, we resubmitted the ARC drawing and shuttering drawing on 29-May-2025. • The structural drawing related to the Ground Floor Beam was submitted on 2-June-2025. • Structure dwg and DBR submitted on 04.06.2025 • Comments shared on Arch dwg on 05.06.2025 and structural dwg via mail on 05.06.25 • Revised Arch dwg submitted on 06.06.2025. • MEPF dwg submitted on 12.06.2025 • Comments given by AE on
-----	---	--

Item No (as per Sch-G)	Item	Status
		<p>14.06.2025.</p> <ul style="list-style-type: none"> • Revised Arch dwg submitted on 17.06.2025 • Conditional Approval upto Terrace level shared on 21.06.2025 • MEPF Comments shared by AE on 21.06.2025. • Discussion on Structural dwgs (Beam and Staircase) on 24.06.25 & 25.06.25. • Re-Submission of MEP Drawings of Building 9B&19E. (Ref- Lr No: RPP-SM-JV-RRW/456 dt 28-06-2025). • Submission of Structure Drawing of 9B & 19E Building (Staircase, GF Slab & Beam). (Ref- Lr. No. RPP-SM-JV/RRW/459 dt- 30-06-2025)
	6m wide FOB for Arrival.	After approval for change of scope for shifting OHE masts and other utilities is accorded (Ref: Contractor's Lr No: 270 dt 08-April-25), the further process will start
	6m wide FOB for Departure.	

Item No (as per Sch-G)	Item	Status
2.7	External Dev Wks for City Side, Rear Side & MEP, Civil, other than Civil, S&T, PA systems	<ul style="list-style-type: none"> • Authority to approve the additional rates for the relocation of entire rear side utilities as they are not in the scope of the contract. • Trees cutting, buildings demolition and Utility Shifting in progress. • However, infringing utility shifting is progressing at slow pace for want of approval for change of scope for shifting utility shifting. Referred to AE through many references. • Work will go on in a meaningful way only after the said approval is accorded. • Contractor submitted the Road and Drain PNP for the rear side on 11-February-2025. • AE's observation letter was received on 19-February-2025. • Contractor submitted a response letter on 8-April-2025. • AE's observation letter was received on 19-April-2025. • Contractor submitted the revised drawing on 17-May-2025. • One-on-one discussion was held on 20-May-2025. • AE's letter was received on 21-May-2025. • Contractor submitted a response letter with Drgs on 23-May-2025. • Structure comments on road shared on 05.06.2025 via mail. • Comments shared via mail on 07.06.2025. • Revised drawings and documents shared on 11.06.2025 via mail. • Comments shared on 15.06.2025. • Revised Documents and drawings shared to AE on 18.06.2025. • Revised final drawings shared to AE on 25.06.2025. •

Item No (as per Sch-G)	Item	Status
2.8	Service Bldg-19A	<ul style="list-style-type: none"> • Preliminary Drgs approved. • Detailed plans will be prepared after the issues connected with master plan are resolved and master plan is approved. • Master plan submitted vide contractor's Lr No: 291 dt 22-April-25 and 147 dt 15-Nov-24.

Item No (as per Sch-G)	Item	Status
2.9	Crew Lobby + TTE Rest Room - 19C (Rear Side)	<ul style="list-style-type: none"> • Geo-Tech investigations done. • Preliminary Drgs approved. • Further works will be started after the plot is handed over (Ref: Contractor's Lr No: 285 dt 18-April-25). • Contractor submitted a letter to the AE's on 24-April-2025 regarding all drawings. • One-on-one discussions were held on 29-April-2025, 30-April-2025, and 1-May-2025. • ARC and STR drawings were submitted via email on 3-May-2025 and 10-May-2025 respectively, for AE's review. • One-on-one discussions were held again on 20-May-2025 and 21-May-2025. • The revised ARC drawing was submitted on 22-May-2025. • The revised STR drawing was submitted on 24-May-2025. • We submitted the 3D elevation on 26-May-2025. • AE's reply was received on 29-May-2025. • Approval for IIT Vetting on 02.06.25 via mail. • Conditional approval was granted by AE on 3-June-2025. • Revised Arch drawings submitted on 06.06.25. • Submission of 3D Elevation drawings on 10.06.25 • Conditional Approval on Arch drawings upto Terrace-16.06.25. • Submitted IIT Vetted Structural dwg upto plinth level on 12.06.25 via mail • MEPF Dwg submitted on 12.06.25. • Approval for Structural GFC received on mail on 15.06.25 • Coordinated Clash free BIM submitted on 16.06.25 • Hard copy (IIT Vetted) with Certificate Submitted on 21.06.2025 • MEPF Comment received on 24.06.25 •

Item No (as per Sch-G)	Item	Status
2.10	Misc Works	
	Resurfacing PF	Broad planning has been submitted to AE. It warrants some works beyond the contract cope. Requested for approval for change of scope.
	Parcel + RMS	<ul style="list-style-type: none"> • Prelim Drgs Approved. • Will be planned after the bigger works are brought onto progressing track.
	Reserve Longue	<ul style="list-style-type: none"> • Prelim Drgs Approved. • Will be planned after the bigger works are brought onto progressing track.
	Deluxe Toilet (19H – Rear Side)	<ul style="list-style-type: none"> • Prelim Drgs Approved. • Will be planned after the bigger works are brought onto progressing track.

	P Way Store (19E – Rear Side)	<ul style="list-style-type: none"> • Preliminary drawings for the building were approved. • Final drawing for the foundation of this building was also approved. • Execution of only 60 -70% foundation is possible because the rear side road is passing across the building. • Foundation concreting in progress. • Progress is slow due to presence of a road passing across this plot. This will be demolished after the diversion road is constructed. For diversion road, plan and profile submitted to AE vide Lr No: 273 dt 11-April-25 and AE have given list of the observations on this on 19.04.2025. • The complete set of drawings was submitted to the AE on 10-April-2025. • Discussions were held between PMS and the Contractor's Consultant on 29-April-2025, 30-April-2025, and 1-May-2025. • The Contractor submitted the BIM model to the authorities on 6-May-2025. • The Contractor received a letter from the AE's office on 9-May-2025. • The Contractor submitted a reply letter and structural drawings to the AE on 10-May-2025. • ARC (Architectural) comments were provided by the AE on 21-May-2025, and HVAC comments were provided on 22-May-2025. • One-on-one discussions were held from 20-May-2025 to 23-May-2025. • After incorporating these comments, we resubmitted the ARC drawing and shuttering drawing on 29-May-2025. • The structural drawing related to the Ground Floor Beam was submitted on 2-June-2025. • Structure dwg and DBR submitted on 04.06.2025 • Comments shared on Arch dwg on 05.06.2025 and structural dwg via mail on 05.06.25 • Revised Arch dwg submitted on 06.06.2025. • MEPF dwg submitted on 12.06.2025 • Comments given by AE on
--	-------------------------------	--

Item No (as per Sch-G)	Item	Status
		<p>14.06.2025.</p> <ul style="list-style-type: none"> • Revised Arch dwg submitted on 17.06.2025 • Conditional Approval upto Terrace level shared on 21.06.2025 • MEPF Comments shared by AE on 21.06.2025. • Discussion on Structural dwgs (Beam and Staircase) on 24.06.25& 25.06.25

	OHE, C&W Office (19F – Rear Side)	<ul style="list-style-type: none"> • Geo-Tech Investigations done. • Preliminary Drgs Approved. • Further works can start after the road passing across the plot is diverted. To divert the road, P&P for diverted road is submitted vide Lr No: 273 dt 11-April-25. • First time the drawings for 19F was submitted vide mail dated 24.12.2025 • AE's observations only on the structural drawings vide mail dated 02.01.2025. No observations on • Revised Drawings submission mail dated 15.01.2025 • AE's observations only on the structural drawings vide mail dated 01.02.2025 • 2nd Revision Drawings submission mail dated 04.03.2025 • AE's observations only on the structural drawings vide mail dated 08.03.2025 • Submission of 3rd revision vide No. RPP-SM-JV/RRW/327 dt 27-03-2025. • One to one discussion on the structural drawings with AE's Lead Designer on 27.03.2025 & 28.03.2025 • Submission of 4th revision of the Structural drawings vide Contractor's Lr. No. RPP-SM-JV/RRW/338 dt 04-04-2025. • AE's comprehensive observation vide its Lr No: TL-PMS/RPPS/194 dt 09-04-2025. • Contractor submitted revised drawings vide RPP-SM-JV/RRW/362 Date: 23-04-2025 • One to one discussion happened with AE on 30th April. • The ARC dwg has been submitted AE'S via mail on 3.05.25 • We received observation on ARC dwg on 16.05.25 • One to one discussion held 20 to 23.05.25 • ARC dwg submitted to AE'S on 24.05.25 • Conditional approval up to plinth level given on 03.06.2025 • Revised Arch drawings submitted on 06.06.25. • Structure submitted on 07.06.2025 • Conditional Approval for IIT vetting given on 13.06.2025
--	-----------------------------------	--

Item No (as per Sch-G)	Item	Status
		<ul style="list-style-type: none"> MEPF Dwg submitted on 12.06.25. Coordinated Clash free BIM submitted on 16.06.25. Conditional approval on arch drawing up to terrace given on 21.06.2025 MEPF Comment received on 25.06.25
	RPF Barracks (19G – Rear Side)	<ul style="list-style-type: none"> Preliminary drawings approved Contractor submitted Architectural & Structure drawings vide mail dated 07th March'2025 AE's observations mail dated 11.03.2025 only having observations on structural drawings and keeping mum over the architectural drawings Contractor submitted revised drawings vide Lr. No. RPP-SM-JV/RRW/333 dt 02-04-2025. AE's observations vide Lr No: TL-PMS/RPPS/203 dt 15-04-2025. The contractor submitted drawings on 23-April-2025. One-on-one discussions were held on 29-April-2025, 30-April-2025, and 1-May-2025. The drawings were resubmitted via email on 3-May-2025. One-on-one discussions were held between 20-May-2025 and 22-May-2025. The contractor submitted the revised ARC drawing on 23-May-2025. Conditional Approval upto Plinth given on 06.06.25. Structure Dwg submitted on 07.06.2025. Conditional Approval for IIT Vetting given on 13.05.25 Clash free coordinated BIM model Submitted on 16.06.25
	& other relocated structures.	<ul style="list-style-type: none"> Rear Side UTS/PRS Shifting: Building constructed at relocated area. Other works in progress. Rear side UTS/PRS relocation: Structure work completed & Other works in progress. Utilities diversion plans approved and work in progress.

Item No (as per Sch-G)	Item	Status
2.11	Shifting/Relocation of Existing Utilities, Demolition of Existing Buildings.	<ul style="list-style-type: none"> • Buildings demolished as per contract scope and also beyond the contract scope. Requested for approval for change of scope vide Lr No: 189 dt 13-Dec-25. • 83 Trees relocated. However, relocation of trees is going on at slow pace for want of approval for change of scope. Referred vide contractor's Lr No: • Utilities are getting shifted as per their infringement to the ongoing works like in 9B/19E, 19F, 19G etc. However, they are all awaiting approval of change of scope.
		<ul style="list-style-type: none"> • Master Plan submitted by Contractor on 21.05.25 • ESS GAD, MEPF-Electrical Master Plan submitted on 30.05.25 Submitted • Comments on ESS GAD & Electrical Masterplan 06.06.2025 • Revised Dwgs submitted on 16.06.2025 • Electrical DBR submitted on 30.05.25 • Electrical DBR -Approved on 04.06.2025 • Plumbing & Firefighting DBR Submitted on 05.06.2025 • Comments shared by AE on 13.06.2025 • Comments on Arch DBR given by AE on 18.06.2025 • Revised DBR Submitted on 18.06.2025 • Comments on Plumbing received on 23.06.2025 • Conditional Approval on Firefighting DBR on 23.06.25 • Mechanical DBR (HVAC) Submitted to AE on 14.06.2025 • Comments shared by AE on 23.06.2025

1. Assistance Required:

- a) Request to kindly initiate the shifting of the infringing CSPDCL lines (Ref: Contractor's Letter No. 304 dated 28-May-2025 and Letter No. 42 dated 25-Jul-2024). These electrical lines are obstructing the proposed road alignment on the rear side, particularly near plots 18E, 18K, etc.
- b) Request to please approve cable route plan to enable to commission temporary UTS/PRS so that 1A plot will be available for work (Ref: Contractor's Lr No: 303 dt 28-May-25).
- c) The Concourse and FOB works are among the most critical components of the project. Effective planning and execution of these works are not feasible unless in-principal approval for the change of scope—specifically for shifting the infringing OHE masts and other obstructing utilities—is granted. Early communication of this approval is kindly requested. (Ref: Contractor's Letter No. 292 dated 25-May-2025 and Letter No. 270 dated 08-May-2025).
- d) Request to please accord in-principal approval for change of scope for shifting the infringing utilities (Ref: Contractor's letters No: 296 dt 26-May-25, 294 dt 25-May-25, 292 dt 25-May-25, 274 dt 12-May-25 and 204 dt 28-Jan-24). This is essential to plan the works and to achieve progress.
- e) Request to resolve the issues connected with master plan and accord approval for the revised master plan early to enable the contractor to program the works in a planned way (Ref: Contractor's Lr No: 291 dt 22-May-25 and Lr No: 147 dt 15-Nov-24).
- f) Plot 19G may please be handed over to contractor duly shifting the Railway material lying in this plot (Ref: Contractor's Lr No: 301 dt 28-May-25).
- g) A municipality drain is currently flowing through the project area on the rear side (near plots 18E to 14B). It has been observed that this drain serves as an outlet for water from private buildings. Unless this drain is diverted outside the project area, the development of the road in this section cannot proceed. Your intervention is kindly requested to facilitate its relocation. (Ref: Contractor's Letter No. 301 dated 28-May-2025) Issue of open sewage Lines/storm water drains of private buildings flowing into Railway land (loco colony area near plots 9B, 19E, 19F, 19G location) may please be addressed to facilitate unhindered execution of the project (Ref: Contractor's Lr No: 124 dt 19-Oct-24).
- h) Private encroachments have been identified on the city side, specifically at plots 9C, 14E, 10, and the adjoining road. These encroachments are hindering construction activities. It is requested that the encroachments be removed at the earliest and the respective plots handed over to the contractor to commence work.

(Ref: Contractor's Letter No. 301 dated 28-May-2025)

- i) Request to kindly initiate the relocation of the existing religious structures (temples) within the project area to facilitate unhindered planning and execution of works by the contractor. (Ref: Contractor's Letter No. 238 dated 14-Jan-2025)
- j) Request to kindly provide the Analysis of Rates for determining the cost of tree relocation, as this activity is attracting a change of scope and requires formal rate approval. (Ref: Contractor's Lr No: 191 dt 14-Dec-24).
- k) Request to please accord in-principal approval for change of scope for shifting of utilities like water pipe lines, cables, earthing pits etc which are beyond the scope of the contract (Ref: Contractor's Lr No: 204 dt 28-Jan-25).
- l) BSNL lines are currently passing through the project area and are obstructing ongoing works. It is requested that these lines be shifted at the earliest. BSNL may kindly be pursued to carry out the necessary relocation. (Ref: Contractor's Letter No. 49 dated 02-Aug-2024).
- m) Request to kindly arrange the required block for UTS/PRS at the front side to facilitate the shifting work, preferably during the last week of July.
- n) Request to kindly arrange a 3-hour power block at location 19C during the first week of July, to facilitate the utility shifting works.
- o) Request to kindly arrange a 3-hour power block for Utility Shifting at City Side.
- p) Request to kindly arrange a 4-hour power block on 3rd week of July, 2025.
- q) S&T Utility Shifting drawing to be approved for 1 & 1A.
- r) Request to kindly obtain permission from GSU and PMS authorities for conducting soil testing on Platforms No. 2, 3, 4, and 5. This is essential for proceeding with the geotechnical investigations in those areas.
- s) One Joint Visit to be done for 300 mm Dia pipe Dismantling at rear Side.
- t) Existing FOB Drawing Required to start the work.

2. Attachments:

- a) Annexure-A: List of important submissions made by the contractor to the Authority Engineer during June-2025.
- b) Annexure-B: List of approvals and other important communications received from Authority Engineer during June-2025.
- c) Annexure-C: List of Machinery deployed during June-2025.
- d) Annexure-D: Summary of Executive team deployed during June-2025.
- e) Annexure-E: Summary of Workers Deployment during June-2025.
- f) Weather report for the month of June-25
- g) Annexure-F: Some Photographs of the activities in June-2025.

Thank you and always assuring our best services.

For RPP-SATHYAMOORTHY (JV)

Abhishek Garg
Project Coordinator
(Authorized Signatory)

Copy to:

1. CPM/GSU/R for kind information please.
2. Dy CE/GSU/R for kind information please.
3. Head Office, RPP Infra Projects Ltd, Email- tender.bo@rppipl.com and project@rppipl.com - For information please.

Annexure-A**Important Submissions made by contractor to AE in the month of June-2025**

No.	Lr Dt	Lr No	Subject Conveyed
1	30-Jun-2025	459	Submission of Structure Drawing of 9B & 19E Building (Staircase, GF Slab & Beam).
2	30-Jun-2025	458	Revised submission of MEPF Master Plan (Electrical) and General Arrangement Drawing (GAD) of City side & Rear Side ESS.
3	28-Jun-2025	457	Re-Submission of Architecture Definitive Drawings for the Rear side Station Building 1-A.
4	28-Jun-2025	456	Re-Submission of MEP Drawings of Building 9B&19E.
5	27-Jun-2025	455	Approved General Arrangement Drawing (GAD) of Buildings.
6	25-Jun-2025	454	Implementation of Project Management Information System (PMIS).
7	24-Jun-2025	453	Submission of Approved hard copy of Electrical Design Basis Report (DBR)-Reg.
8	24-Jun-2025	452	Submission of Definitive Drawing of Storm water drainage layout.
9	21-Jun-2025	451	Revised Based Line Programme.
10	20-Jun-2025	450	Conditional approval up to terrace level of 9B & 19E (Architecture) building.
11	20-Jun-2025	449	Submission of 19C Structure (IIT-vetted) drawing and Certificate.
12	19-Jun-2025	448	Request to approval shifting of S&T cable for Excavation & construction of 1A Building
13	19-Jun-2025	447	Request to approval Cable Route Plan for laying OFC & other cables to Temporary UTS PRS building on front side.
14	19-Jun-2025	446	Re-Submission of Bank Account Details & Documents for processing of the bill.
15	18-Jun-2025	445	Submission of Revised Plumbing & Firefighting DBR(R-2).
16	17-Jun-2025	444	Request to hand over of UTS PRS building rear side.
17	17-Jun-2025	443	Re-Submission of Architecture Definitive Drawing set of 9B (MMTH) & 19E (P-way store).R-04
18	17-Jun-2025	442	Submission of Compliance of road and drain on rear side of station building.
19	16-Jun-2025	441	Submission of 19F, 19G and 19C BIM Model.
20	16-Jun-2025	440	Revised submission of MEPF Master Plan (Electrical) and General Arrangement Drawing (GAD) of City side & Rear Side ESS.
21	16-Jun-2025	439	Submission of Detailed MEP Drawing- 19F Building.
22	14-Jun-2025	438	Submission of Mechanical Design Basis Report (DBR) Rev R-2 Reg.

23	13-Jun-2025	437	Submission of Bank Account details
24	10-Jun-2025	436	Submission of two more elevation options for 19C building..
25	12-Jun-2025	435	Submission of MEPF drawings of 9B 19E Building. (1)
26	12-Jun-2025	434	Submission of MEPF drawings of 19C Building.
27	12-Jun-2025	433	Request for 4 Hour Block Allocation for Shifting to Temporary UTSPRS Building rear side
28	12-Jun-2025	432	Submission of Final Geotechnical Investigation Report.
29	10-Jun-2025	431	Submission of 2nd RA Bill - Raipur SECR Project
30	09-Jun-2025	430	Removal of boundary wall at ch. 0+120- ch.0+140
31	10-Jun-2025	428	Submission of Detailed Drawing of Air Concourse.
32	07-Jun-2025	427	Non-availability of Engineer/Team (S&T).
33	07-Jun-2025	426	Submission of 19F- (OHE PSI TRD Office Building Detailed Design & Drawings.
34	07-Jun-2025	425	Submission of Detailed Design and Drawings-19G RPF Barrack.
35	07-Jun-2025	424	Submission of Monthly Stage Payment Statement for Works.
36	06-Jun-2025	423	Re-Submission of Architecture Definitive Drawing set of 9B (MMTH) &19E (P-way store).
37	06-Jun-2025	422	Submission of 19F- (OHE PSI TRD Office Building Definitive Drawings.
38	06-Jun-2025	421	Submission of 19C (Crew Lobby & TTE Rest Room) Definitive Drawing. Stage(R4).
39	05-Jun-2025	420	Submission of Plumbing & Firefighting DBR(R1).
40	05-Jun-2025	419	Pending MEPF Design & Drawings for compliance.
41	05-Jun-2025	418	Submission of revised 1st RA Bill.
42	05-Jun-2025	417	Submission of MPR for May - 2025
43	04-Jun-2025	416	Submission herewith the proposed breakup of Schedule-G.
44	02-Jun-2025	415	Submission of Structure Definitive Drawing set of 9B (MMTH) & 19E (P--Way store)

Annexure-B

**Important Communications received from Authority / Authority Engineer during
June-2025**

No.	Lr Dt	Lr No	Subject Conveyed
1	24-Jun-2025	308	Submission of Quality Assurance Plan (QAP) for various works related to the project.
2	23-Jun-2025	306	Observations of HVAC Design Basis Report (DBR) Rev-02.
3	23-Jun-2025	307	Observations of Plumbing & Firefighting Design Basis Report (DBR) Rev-02.
4	21-Jun-2025	304	Conditional approval up to terrace level of 19F (Architecture) building subject to incorporation of final elevations & comments.
5	20-Jun-2025	303	Delay in submission of DSC for bill entry and acceptance of bill format.
6	19-Jun-2025	302	Conditional approval up to terrace level of 9B & 19E (Architecture) building subject to incorporation of final elevations & comments.
7	18-Jun-2025	299	Review of Base Line Program as on 16.06.2025
8	18-Jun-2025	300	Observation on Architecture drawing of Air Concourse.
9	18-Jun-2025	301	Observations on Architecture Design Basis Report (DBR).
10	15-Jun-2025	297	3D view of Crew lobby office and TTE rest room and other buildings 15.06.2025.
11	15-Jun-2025	298	Requirement of 4hrs block for shifting of rear side UTS PRS 15.06.2025.
12	14-Jun-2025	294	Observations on Geotechnical Investigation reports 14.06.2025
13	14-Jun-2025	295	Observations on Architectural Drawings of 9B 19E 14.06.2025
14	14-Jun-2025	296	Conditional Approval for 19C Architectural drawings (Upto Terrace Level) 14.06_2025
15	13-Jun-2025	293	Observations on Plumbing & Firefighting DBR Rev-01
16	07-Jun-2025	291	Non-availability of Engineer/Team (S&T).
17	06-Jun-2025	288	Regarding observations in Electrical drawings of New ESS on both sides.
18	06-Jun-2025	290	Conditional approval up to plinth level of 19G (Architecture) building subject to incorporation of comments.
19	06-Jun-2025	DEE/G SU/R/F -R(EP)	Approval of Electrical design basis report (DBR).

20	05-Jun-2025	285	Observation on Architecture drawing of building No. 19B-19E
21	04-Jun-2025	279	Slow progress of Electrical works.
22	04-Jun-2025	280	Statement regarding hinderance for electrical work.
23	04-Jun-2025	281	Approval of Electrical Design Basis Report (DBR).
24	04-Jun-2025	282	Submission of Monthly Stage Payment Statement for Works.
25	04-Jun-2025	283	Availability of experts as per approval of the Authority.
26	04-Jun-2025	284	Pending MEPF Design & Drawings for compliance.
27	03-Jun-2025	274	Submission of machinery details for station development works.
28	03-Jun-2025	275	3D view of 19C Crew lobby office & TTE Rest room Building and other buildings.
29	03-Jun-2025	276	Conditional approval up to plinth level of 19F (Architecture) building subject to incorporation of comments.
30	02-Jun-2025	273	Conditional approval of up to plinth level of 19C (Architecture) building subject to incorporation of comments.

Annexure-C

List of Machinery deployed during Jun-2025


Dt	DG Sets	Excavator	JCB mounted breaker	JCBs	Tractor Graders	Soil Compactor	Mini Tandem Roller	Tandem Roller	Walk Behind Roller	Hyvas	Water Tankers	Transit Millers	DCM(Tata 712)	Tower Light	LMVs	Batching Plant	Loaders	Trailers	Hydra	Niddle Vibrators	Plate Compactopr	Dewatering Pumps	Steel cutting Machines	Steel Bending Machines	Threading & Forginf	Tractor	Tractor Trolley	Gas Cutter	Welding Machine	Concrete Pump	Bike	Anti Smog Gun	Total
01-Jun-25	2	2	1	2	1	1	1	1	1	5	2	3	1	3	9	1	1	1	2	3	1	15	2	2	1	1	1	2	2	1	9	1	81
02-Jun-25	2	2	1	2	1	1	1	1	1	5	2	3	1	3	9	1	1	1	2	3	1	15	2	2	1	1	1	2	2	1	9	1	81
03-Jun-25	2	2	1	2	1	1	1	1	1	5	2	3	1	3	9	1	1	1	2	3	1	15	2	2	1	1	1	2	2	1	9	1	81
04-Jun-25	2	2	1	2	1	1	1	1	1	5	2	3	1	3	9	1	1	1	2	3	1	15	2	2	1	1	1	2	2	1	9	1	81
05-Jun-25	2	2	1	2	1	1	1	1	1	5	2	3	1	3	9	1	1	1	2	3	1	15	2	2	1	1	1	2	2	1	9	1	81
06-Jun-25	2	2	1	2	1	1	1	1	1	5	2	3	1	3	9	1	1	1	2	3	1	15	2	2	1	1	1	2	2	1	9	1	81
07-Jun-25	2	2	1	2	1	1	1	1	1	5	2	3	1	3	9	1	1	1	2	3	1	15	2	2	1	1	1	2	2	1	9	1	81
08-Jun-25	2	2	1	2	1	1	1	1	1	5	2	3	1	3	9	1	1	1	2	3	1	15	2	2	1	1	1	2	2	1	9	1	81
08-Jun-25	2	2	1	2	1	1	1	1	1	5	2	3	1	3	9	1	1	1	2	3	1	15	2	2	1	1	1	2	2	1	9	1	81
09-Jun-25	2	2	1	2	1	1	1	1	1	5	2	3	1	3	9	1	1	1	2	3	1	15	2	2	1	1	1	2	2	1	9	1	81
10-Jun-25	2	2	1	2	1	1	1	1	1	5	2	3	1	3	9	1	1	1	2	3	1	15	2	2	1	1	1	2	2	1	9	1	81
11-Jun-25	2	2	1	2	1	1	1	1	1	5	2	3	1	3	9	1	1	1	2	3	1	15	2	2	1	1	1	2	2	1	9	1	81
12-Jun-25	2	2	1	2	1	1	1	1	1	5	2	3	1	3	9	1	1	1	2	3	1	15	2	2	1	1	1	2	2	1	9	1	81
13-Jun-25	2	2	1	2	1	1	1	1	1	5	2	3	1	3	9	1	1	1	2	3	1	15	2	2	1	1	1	2	2	1	9	1	81
14-Jun-25	2	2	1	2	1	1	1	1	1	5	2	3	1	3	9	1	1	1	2	3	1	15	2	2	1	1	1	2	2	1	9	1	81
15-Jun-25	2	2	1	2	1	1	1	1	1	5	2	3	1	3	9	1	1	1	2	3	1	15	2	2	1	1	1	2	2	1	9	1	81
16-Jun-25	2	2	1	2	1	1	1	1	1	5	2	3	1	3	9	1	1	1	2	3	1	15	2	2	1	1	1	2	2	1	9	1	81
17-Jun-25	2	2	1	2	1	1	1	1	1	5	2	3	1	3	9	1	1	1	2	3	1	15	2	2	1	1	1	2	2	1	9	1	81
18-Jun-25	2	2	1	2	1	1	1	1	1	5	2	3	1	3	9	1	1	1	2	3	1	15	2	2	1	1	1	2	2	1	9	1	81
19-Jun-25	2	2	1	2	1	1	1	1	1	5	2	3	1	3	9	1	1	1	2	3	1	15	2	2	1	1	1	2	2	1	9	1	81
20-Jun-25	2	2	1	2	1	1	1	1	1	5	2	3	1	3	9	1	1	1	2	3	1	15	2	2	1	1	1	2	2	1	9	1	81

Dt	DG Sets	Excavator	JCB mounted breaker	JCBs	Tractor Graders	Soil Compactor	Mini Tandem Roller	Tandem Roller	Walk Behind Roller	Hyvass	Water Tankers	Transit Millers	DCM(Tata 712)	Tower Light	LMVs	Batching Plant	Loaders	Trailers	Hydra	Niddle Vibrators	Plate Compactopr	Dewatering Pumps	Steel cutting Machines	Steel Bending Machines	Threading & Forginf	Tractor	Tractor Trolley	Gas Cutter	Welding Machine	Concrete Pump	Bike	Anti Smog Gun	Total
21-Jun-25	2	2	1	2	1	1	1	1	1	5	2	3	1	3	9	1	1	1	2	3	1	15	2	2	1	1	1	2	2	1	9	1	81
22-Jun-25	2	2	1	2	1	1	1	1	1	5	2	3	1	3	9	1	1	1	2	3	1	15	2	2	1	1	1	2	2	1	9	1	81
23-Jun-25	2	2	1	2	1	1	1	1	1	5	2	3	1	3	9	1	1	1	2	3	1	15	2	2	1	1	1	2	2	1	9	1	81
24-Jun-25	2	2	1	2	1	1	1	1	1	5	2	3	1	3	9	1	1	1	2	3	1	15	2	2	1	1	1	2	2	1	9	1	81
25-Jun-25	2	2	1	2	1	1	1	1	1	5	2	3	1	3	9	1	1	1	2	3	1	15	2	2	1	1	1	2	2	1	9	1	81
26-Jun-25	2	2	1	2	1	1	1	1	1	5	2	3	1	3	9	1	1	1	2	3	1	15	2	2	1	1	1	2	2	1	9	1	81
27-Jun-25	2	2	1	2	1	1	1	1	1	5	2	3	1	3	9	1	1	1	2	3	1	15	2	2	1	1	1	2	2	1	9	1	81
28-Jun-25	2	2	1	2	1	1	1	1	1	5	2	3	1	3	9	1	1	1	2	3	1	15	2	2	1	1	1	2	2	1	9	1	81
29-Jun-25	2	2	1	2	1	1	1	1	1	5	2	3	1	3	9	1	1	1	2	3	1	15	2	2	1	1	1	2	2	1	9	1	81
30-Jun-25	2	2	1	2	1	1	1	1	1	5	2	3	1	3	9	1	1	1	2	3	1	15	2	2	1	1	1	2	2	1	9	1	81
Total	60	60	30	60	30	30	30	30	30	150	60	90	30	90	270	30	30	30	60	90	30	450	60	60	30	30	30	60	60	30	270	30	2430


Annexure-D
Executive Deployed during June- 2025

No	Grade of Executive	Overall	MEP	Structures	OHE	Electrical	S&T	HIGHWAY	QC/QA	Survey	IT	Ptg & Billing	HSE	Stores	HR & Admin	P&E	Security	Total
1	SPM	1																1
2	APM	1																1
3	Asst Manager/Manager/ Sr Manager		1				1	1	1	0		1	2		1			8
4	Sr Engineer/Engineer			3	1	2		1	1	2		1				1		13
5	Jr Engineer/ Supervisor/ Technician/ GET/DET/Executive		2	8		3	1	1	2		1	3	1	5	2	3	1	30
6	Vehicle Drivers / Plant Operators												1			50		50
7	Helpers					1			3	3		2	1	2	12			24
8	Guard/Supervisors															27	27	
	Total →	2	3	11	1	6	2	3	7	5	1	5	5	7	5	66	28	157

Annexure-E
Weather Report during June-25

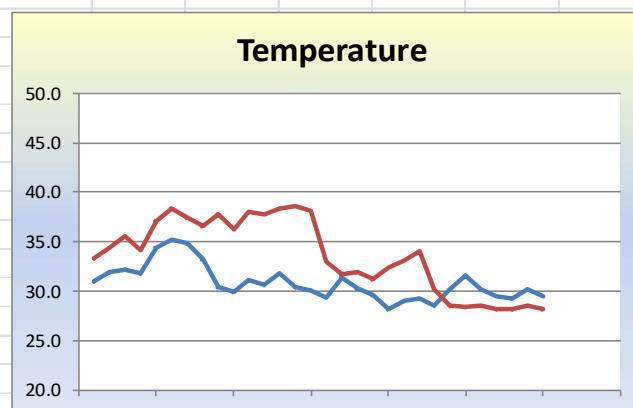WEATHER REPORT								GRAPHICAL REPRESENTATION		
SL No	Date	Temperature (Celsius)		Humidity (%)		Rainfall (mm)	Cumulative Rain fall (mm)	Climatic Details		
		Min	Max	Min	Max					
1	01.06.2025	31.0	33.3	57	61	0.00	0.00	Sunny		
2	02.06.2025	31.9	34.4	48	52	0.00	0.00	Sunny		
3	03.06.2025	32.2	35.6	46	50	0.00	0.00	Sunny		
4	04.06.2025	31.8	34.2	49	54	0.00	0.00	Sunny		
5	05.06.2025	34.4	37.1	53	64	0.00	0.00	Sunny		
6	06.06.2025	35.2	38.4	56	63	0.00	0.00	Sunny		
7	07.06.2025	34.8	37.4	58	65	0.00	0.00	Sunny		
8	08.06.2025	33.2	36.6	40	50	0.00	0.00	Sunny		
9	09.06.2025	30.4	37.8	42	56	0.00	0.00	Sunny		
10	10.06.2025	29.9	36.3	48	57	45.00	45.00	Rainy		
11	11.06.2025	31.1	38.0	37	51	0.00	45.00	Sunny		
12	12.06.2025	30.6	37.8	40	52	0.00	45.00	Sunny		
13	13.06.2025	31.8	38.4	38	54	0.00	45.00	Sunny		
14	14.06.2025	30.4	38.6	37	56	0.00	45.00	Sunny		
15	15.06.2025	30.1	38.1	36	58	15.00	60.00	Drizzling		
16	16.06.2025	29.4	33.0	46	52	0.00	60.00	Sunny		
17	17.06.2025	31.4	31.7	48	49	0.00	60.00	Sunny		
18	18.06.2025	30.3	31.9	49	51	0.00	60.00	Sunny		
19	19.06.2025	29.6	31.2	52	56	0.00	60.00	cloudy		
20	20.06.2025	28.2	32.4	53	57	0.00	60.00	cloudy		
21	21.06.2025	29.0	33.1	51	54	0.00	60.00	cloudy		
22	22.06.2025	29.3	34.0	43	55	0.00	60.00	cloudy		
23	23.06.2025	28.5	30.2	61	63	0.00	60.00	cloudy		
24	24.06.2025	30.2	28.5	61	63	0.00	60.00	cloudy		
25	25.06.2025	31.6	28.4	53	58	0.00	60.00	cloudy		
26	26.06.2025	30.2	28.5	56	60	45.00	105.00	rainy		
27	27.06.2025	29.5	28.2	54	58	30.00	135.00	Rainy & Cloudy		
28	28.06.2025	29.2	28.2	54	58	30.00	165.00	Rainy & Cloudy		
29	29.06.2025	30.2	28.5	56	60	45.00	210.00	rainy		
30	30.06.2025	29.5	28.2	54	58	30.00	240.00	Rainy & Cloudy		
		Total Rainfal During The Month				240				

Some Photographs of the activities done during Jun-25
19 C Footing Column :Casting ,Curing Work

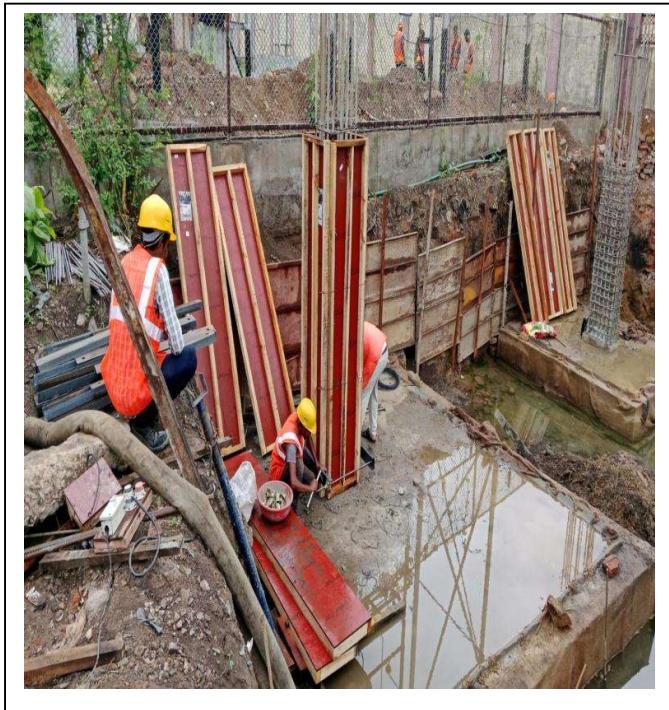


Subgrade Preparation Work Is in Progress



WMM Bed Preparation & Compaction Work Is In Progress





Temporary Parcel Office Work In Progress

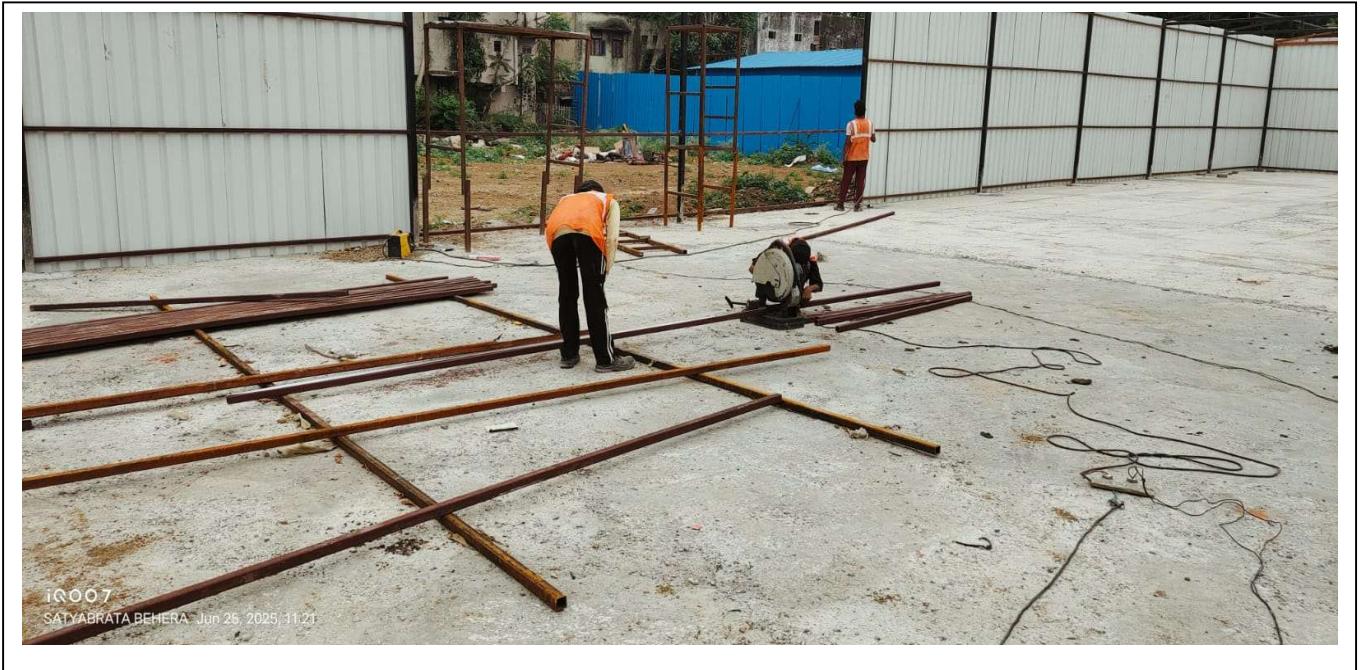

Tree Shifting Work Is In Progress From RPF Colony to WRS



9B & 19E Footing Raft & Column Casting

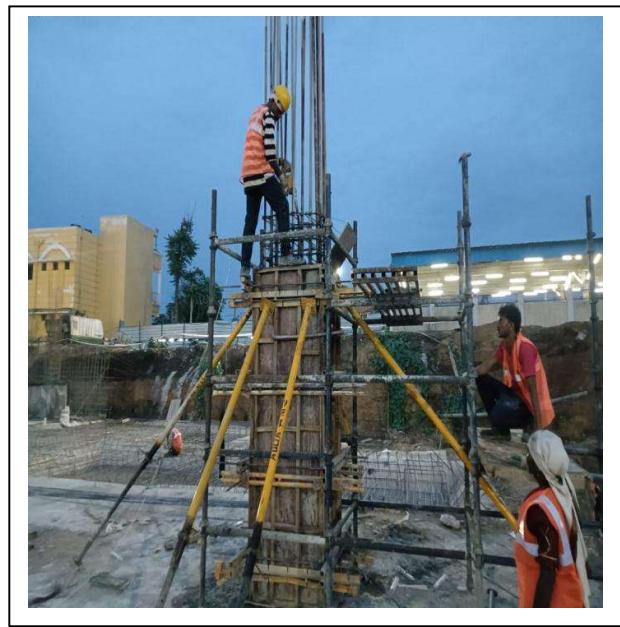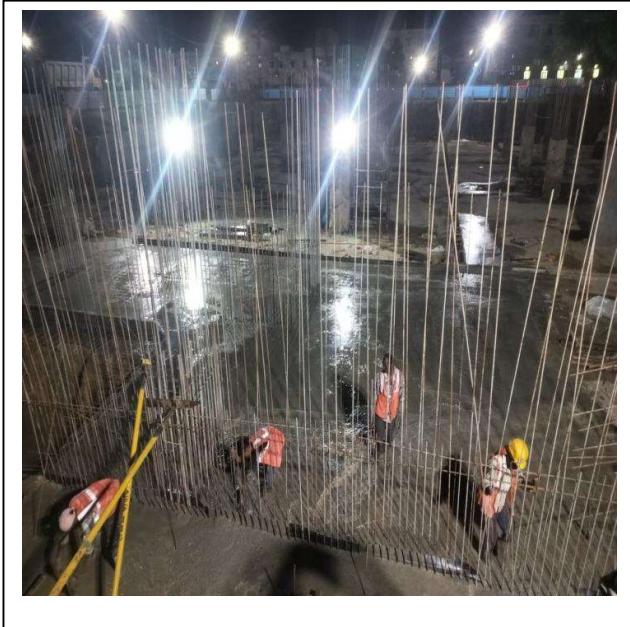

9B & 19E Slab Shuttering Work In Progress



9B & 19E Retaining Wall Work In Progress



19F Column & Footing Steel Binding Work In Progress



Electrical Chamber Brick Wall Work In Progress CH 0+400



Borehole Drilling Work In Progress at FOB Location



Excavation Of Trench For Shifting Of Existing Live Cable at 1A Work in Progress



Gi Pipe 50mm Dia Laying at 19C Building Area



Gi Pipe 8mm Dia Laying Work IS In Progress



Sand Filing in Progress at HT Cable trench



Laying of HT Cable for UTS/PRS City Side



(H.T Cable Trench Work at 19C Area(Under 33KV)



H.T Over Head Line Dismantling Work



(Daily Review Meeting Conducted at Camp)



(Daily Review Meeting Conducted at Camp)



(Daily Review Meeting Conducted at Camp)



Safety Induction Training Conducted to new Workmen



Safety checking of Power tools



Daily Morning Toolbox Talk at site Before starting day's work




UTS PRS Successfully Handover





Catch Net Fixed at 9B Area

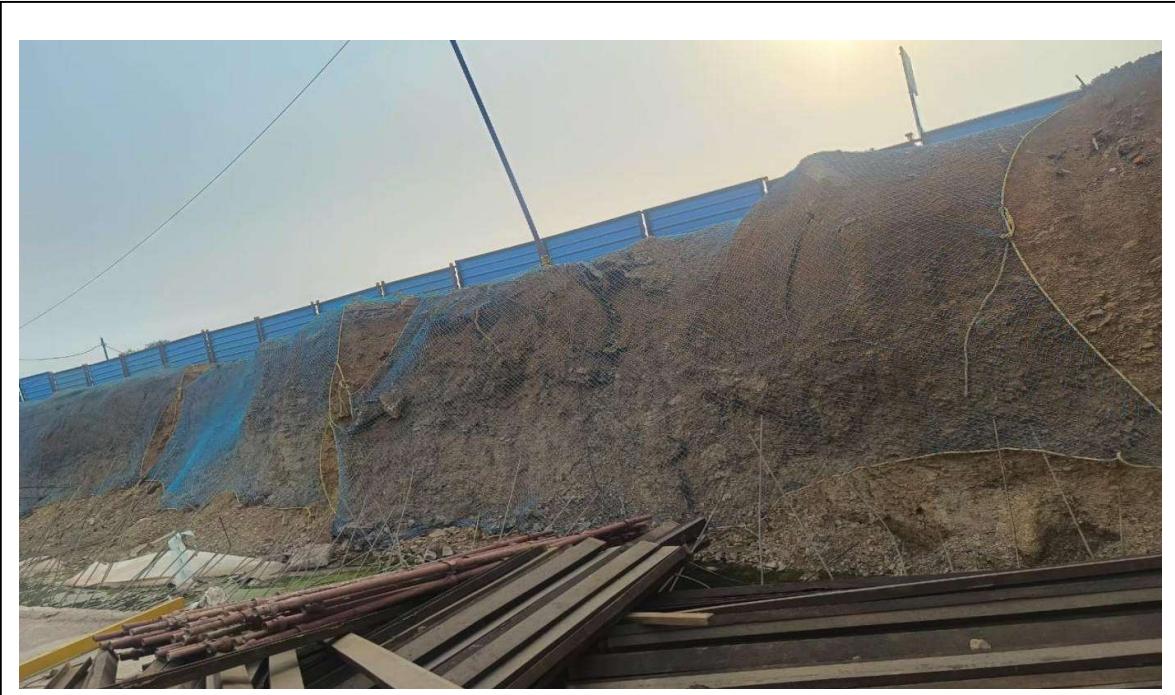

Fire Safety Arrangement at Site



Movable Barricades Placed Near Borehole at PF-7

